

Agenda

1. Review timings against project plan
2. Review planning conditions
3. Traffic
4. Noise
5. Security
6. Restoration
7. Communications
8. Complaints
9. Next meeting

I Review timings against project plan

Civils site preparation works commenced at the Wellsite 5th May 2009 and were completed 17th June 2009.

Mobilisation of the drilling rig commenced 18th June 2009 and was largely complete by 30th June 2009. However, an unforeseen maintenance issue has arisen with the main generators and the hydraulic power system which is causing a delay to the commencement of drilling.

The following key durations continue to be planned, assuming one well is drilled.

No	Activity	Duration (days)	Duration (weeks)	Working hours
1	Rig mobilisation	completed		
2	Drilling - reach target location	70	11.7	24/7
3	Drilling - log and run liner	12		24/7
4	Rig demobilisation	16	3.2	Mon-Fri 0800-1830 (Sat 0800-1300)

Planned drilling durations, assuming one well

The appraisal testing programme is under review at present and will be refined once drilling is underway.

Refer to Appendix I for the current target programme (which assumes drilling commences mid-July 2009).

2 Review planning conditions

The planning permission was granted with 36 conditions. All conditions are being managed and monitored by Star Energy.

Since the Albury Working Group meeting of 23rd March 2009, all subsequent planning condition submissions requiring consultation have been copied to Joanna Cadman, Clerk to Albury Parish Council, for circulation to the Albury Working Group.

4 conditions require notifications to SCC:

Condition	Notification Required	Submitted	Status
2	Within 7 days of commencement of site preparation.	11/5/09	No further action required.
4	Within 7 days of commencement of drilling.	-	Submission pending commencement of drilling. Also, clarification on wording of condition requested from SCC.
5	Within 7 days of commencement of flaring.	-	Submission not yet required.
36	Once the overall restoration planting and seeding is complete.	-	Submission not yet required.

7 conditions require submissions to SCC:

Condition	Key Issue	Submitted	Approved	Notes
11	Protection of the water environment	30/4/09 (civils only)	-	Environment Agency (EA) queries being addressed.
		- (drilling only)	-	Details for drilling being discussed with the EA.
		- (testing only)	-	Details for testing to be submitted before testing commences.
14	Traffic Management Plan (TMP)	17/4/09	n/a	No further action required. Star Energy and their Contractors are proactively managing the TMP.
18	Breeding Birds	27/2/09	5/6/09	No further action required unless additional surveys are required because of any hiatus in activity between drilling, testing, restoration.
19	Badgers	17/2/09	24/2/09	No further action required.

20	Bats	17/2/09	5/6/09	No further action required.
22	Newts	24/3/09	-	SCC approval overdue.
24	Car Park Restoration	4/6/09	-	SCC approval anticipated August 2009.

3 Traffic

3.1 Drilling Rig Trailer

The HGV traffic routes for the Rig Mobilisation and Rig Demobilisation Phases and the Drilling Phase were presented at the previous Albury Working Group Meeting No 4 on 8th June 2009.

Arrival of the drilling rig trailer took place on 18th June 2009. An email and photograph was emailed to Joanna Cadman and Nick Wenman on 22nd June 2009 as per Appendix 2.

3.2 Traffic Management Plan

Traffic management has been going well to date and the Traffic Management Plan is being strictly complied with. Star Energy will continue to proactively manage the project traffic.

3.3 Photographic Surveys

A total of seven photographic surveys have taken place to date. The first survey on 30th April was accompanied by John Brockwell who advised the locations to be recorded. No significant discrepancies have been noted to date. The surveys will continue to be carried out as previously agreed with the next one due mid-late July 2009.

3.4 Main contractors during drilling

At the previous Albury Working Group Meeting No 4 on 8th June 2009, Star Energy were requested to supply a list of contractors whose vehicles will be engaged during the mobilisation and drilling stages. This list is provided as follows:

During drilling rig mobilisation the main contractors were:

- Williams Shipping for miscellaneous loads during rig move
- Marsh Plant for cranes

During drilling the following main contractors will be utilised:

- Williams Shipping for miscellaneous drilling equipment
- Grampian International for miscellaneous drilling equipment

- Halliburton for cementing services
- MI Swaco for mud materials
- BKP for waste management
- Walker and Sons Haulier for miscellaneous
- Rocon for civil materials
- Schlumberger for logging services
- Foulkes for drilling fluids
- FBG for waste management
- Wessex for fuel
- Marsh Plant for cranes

4 Noise

The noise monitoring continues to go well and there has been no known exceedance of the planning conditions noise limits.

The noise monitoring programme includes:

- a site microphone linked to a computer which provides 'real time' traffic light style warnings if there is any likelihood of noise conditions being exceeded over any half-hour period;
- weekly visits by acoustics consultants who visit the Wellsite and key properties several times over the course of a day;

5 Security

There have been no security issues at the Wellsite.

6 Restoration

Apart from the recent submission to Surrey County Council regarding Planning Condition 24 and restoration of the temporary access track car park, there is no change to the overall restoration plans since the last Albury Working Group meeting.

7 Communications

The communications programme is progressing as follows:

- personal contact is being maintained with residents at The Bungalow and Keepers Cottage and being sought with the residents of Park Road
- a 24-hour complaint line continues to operate
- the general Star Energy information line continues to be available in work hours
- the project website has been updated in line with progress and now carries working group reports and minutes. Progress photos will be added shortly.
- a news release is being prepared re the translocation of newts to Chilworth School
- an update can now be provided as required for the parish newsletter and website

7.1 Other community activity

The Star Energy Community Fund has now dispensed 2009/10 grants to:

- Albury Parish Council for its village enhancement project (£10,000)
- Albury Old Parish Church for Albury Flower Festival (held mid June) (£2,500)
- Relate West Surrey for the Relateen youth counselling project (£6,200)
- Blackheath Church Mural Restoration (£9,000)
- Shere Recreation Ground improvements (£9,000 agreed but yet to be dispensed)

Star Energy has separately contributed £500 towards the costs for the Albury Village Weekend (18 -19 July).


8 Complaints

No complaints have been received to date.

9 Next meeting

The first or last week of August is suggested as suitable timing for the next meeting.

Appendix 1 - Appraisal Drilling target dates

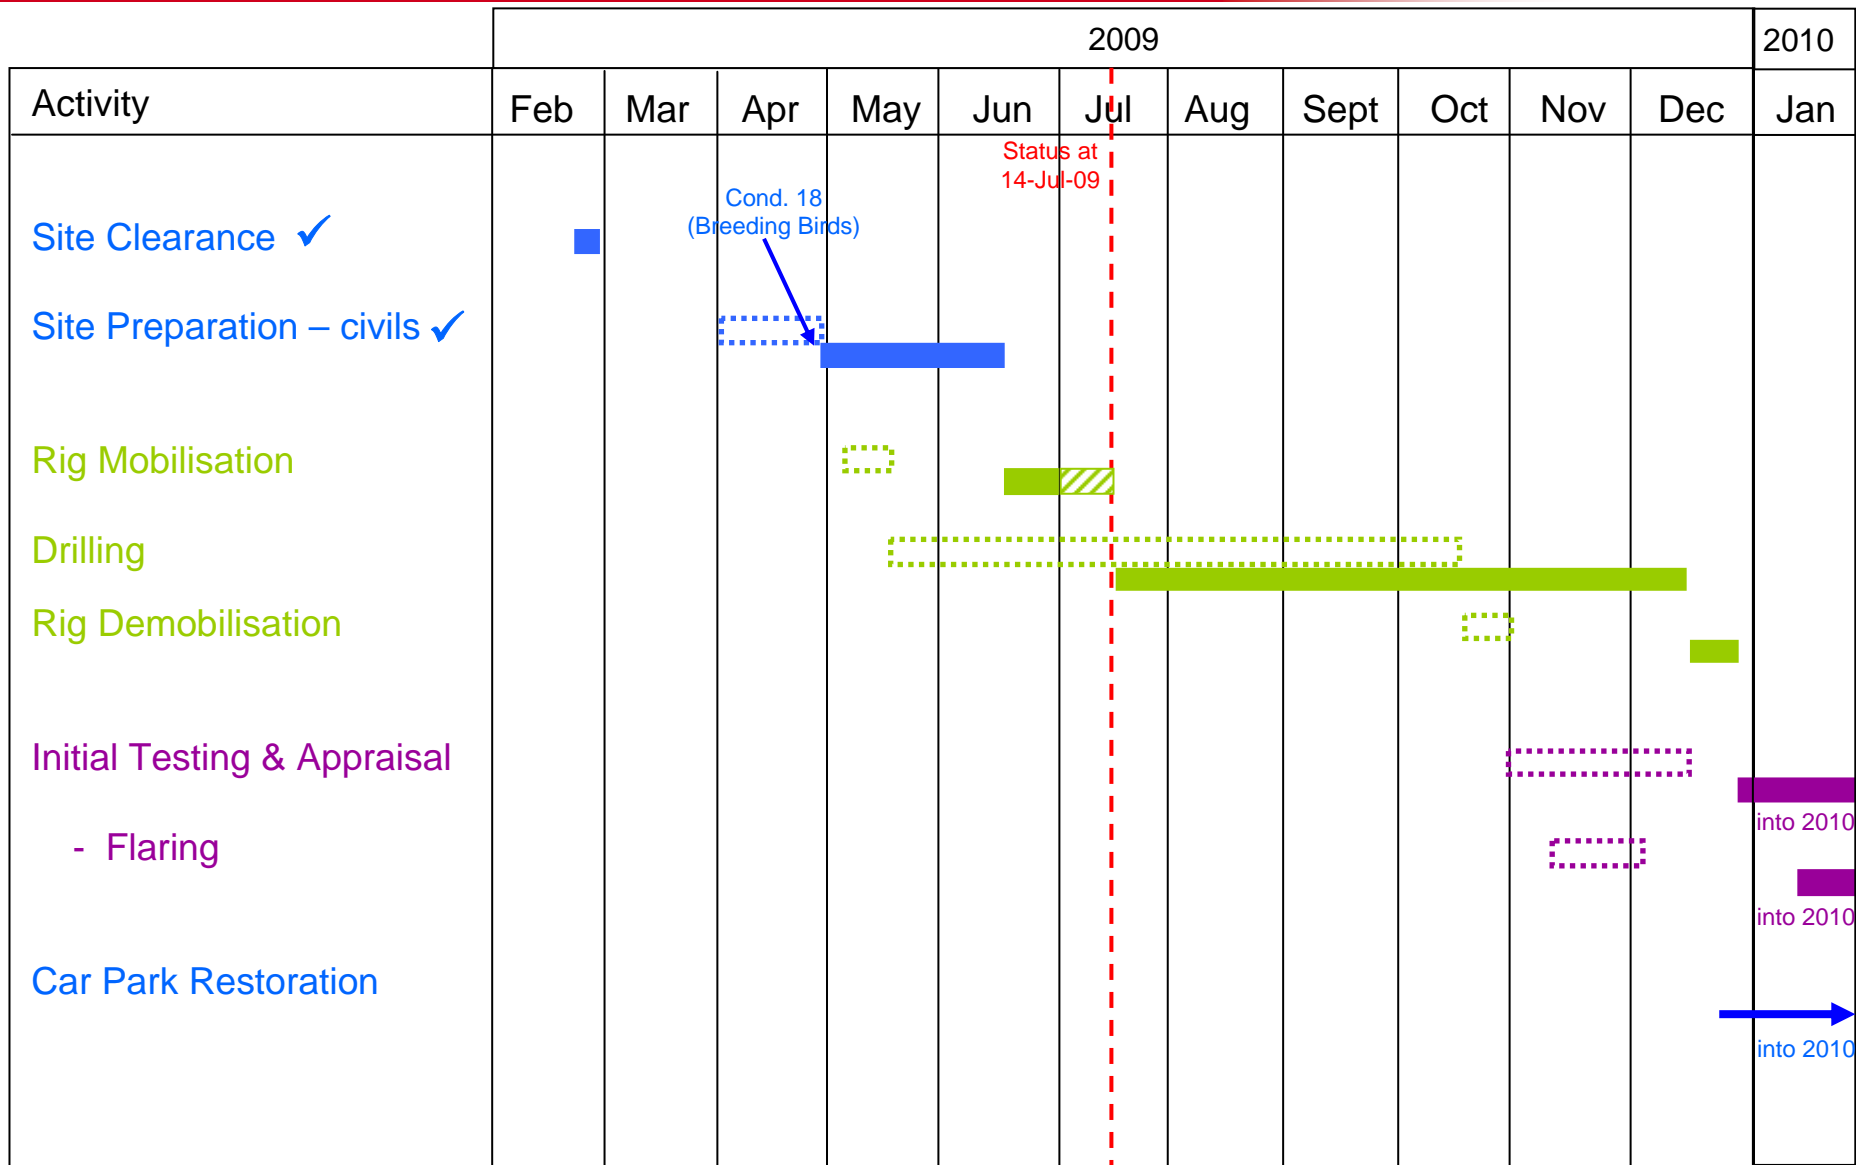

Appendix 2**Sophie Tucker**

From: Sophie Tucker
Sent: 22 June 2009 14:07
To: 'Nick Wenman'
Cc: joanna@joannacadman.com; Barrie Hedges
Subject: Albury Appraisal - arrival of rig trailer
Attachments: Rig trailer arrival 080609.pdf

Dear Nick,

I thought you would be interested to know that our rig trailer arrived last Thursday morning at 11.19am. John Brockwell stopped by, and along with Cathy Goddard and her son Philip, we watched it come up New Road and enter the wellsite entrance off New Road. The attached photo shows it turning off New Road.

Kind regards,
Sophie

Sophie Tucker
Senior Project Engineer

Star Energy Group plc
Humbly Grove Oilfield,
Weston Common, The Avenue
Lasham, Alton, Hampshire GU34 5SY

t: 01256 38 4484 / m: 07786 065152 / sw: 01256 38 1621 / f: 01256 38 1524
e: stucker@starenergy.co.uk

Appendix 2

Star Energy Albury Park Wellsite - Appraisal Drilling Project

Arrival of rig trailer at 11.19am on Thursday 18th June 2009

